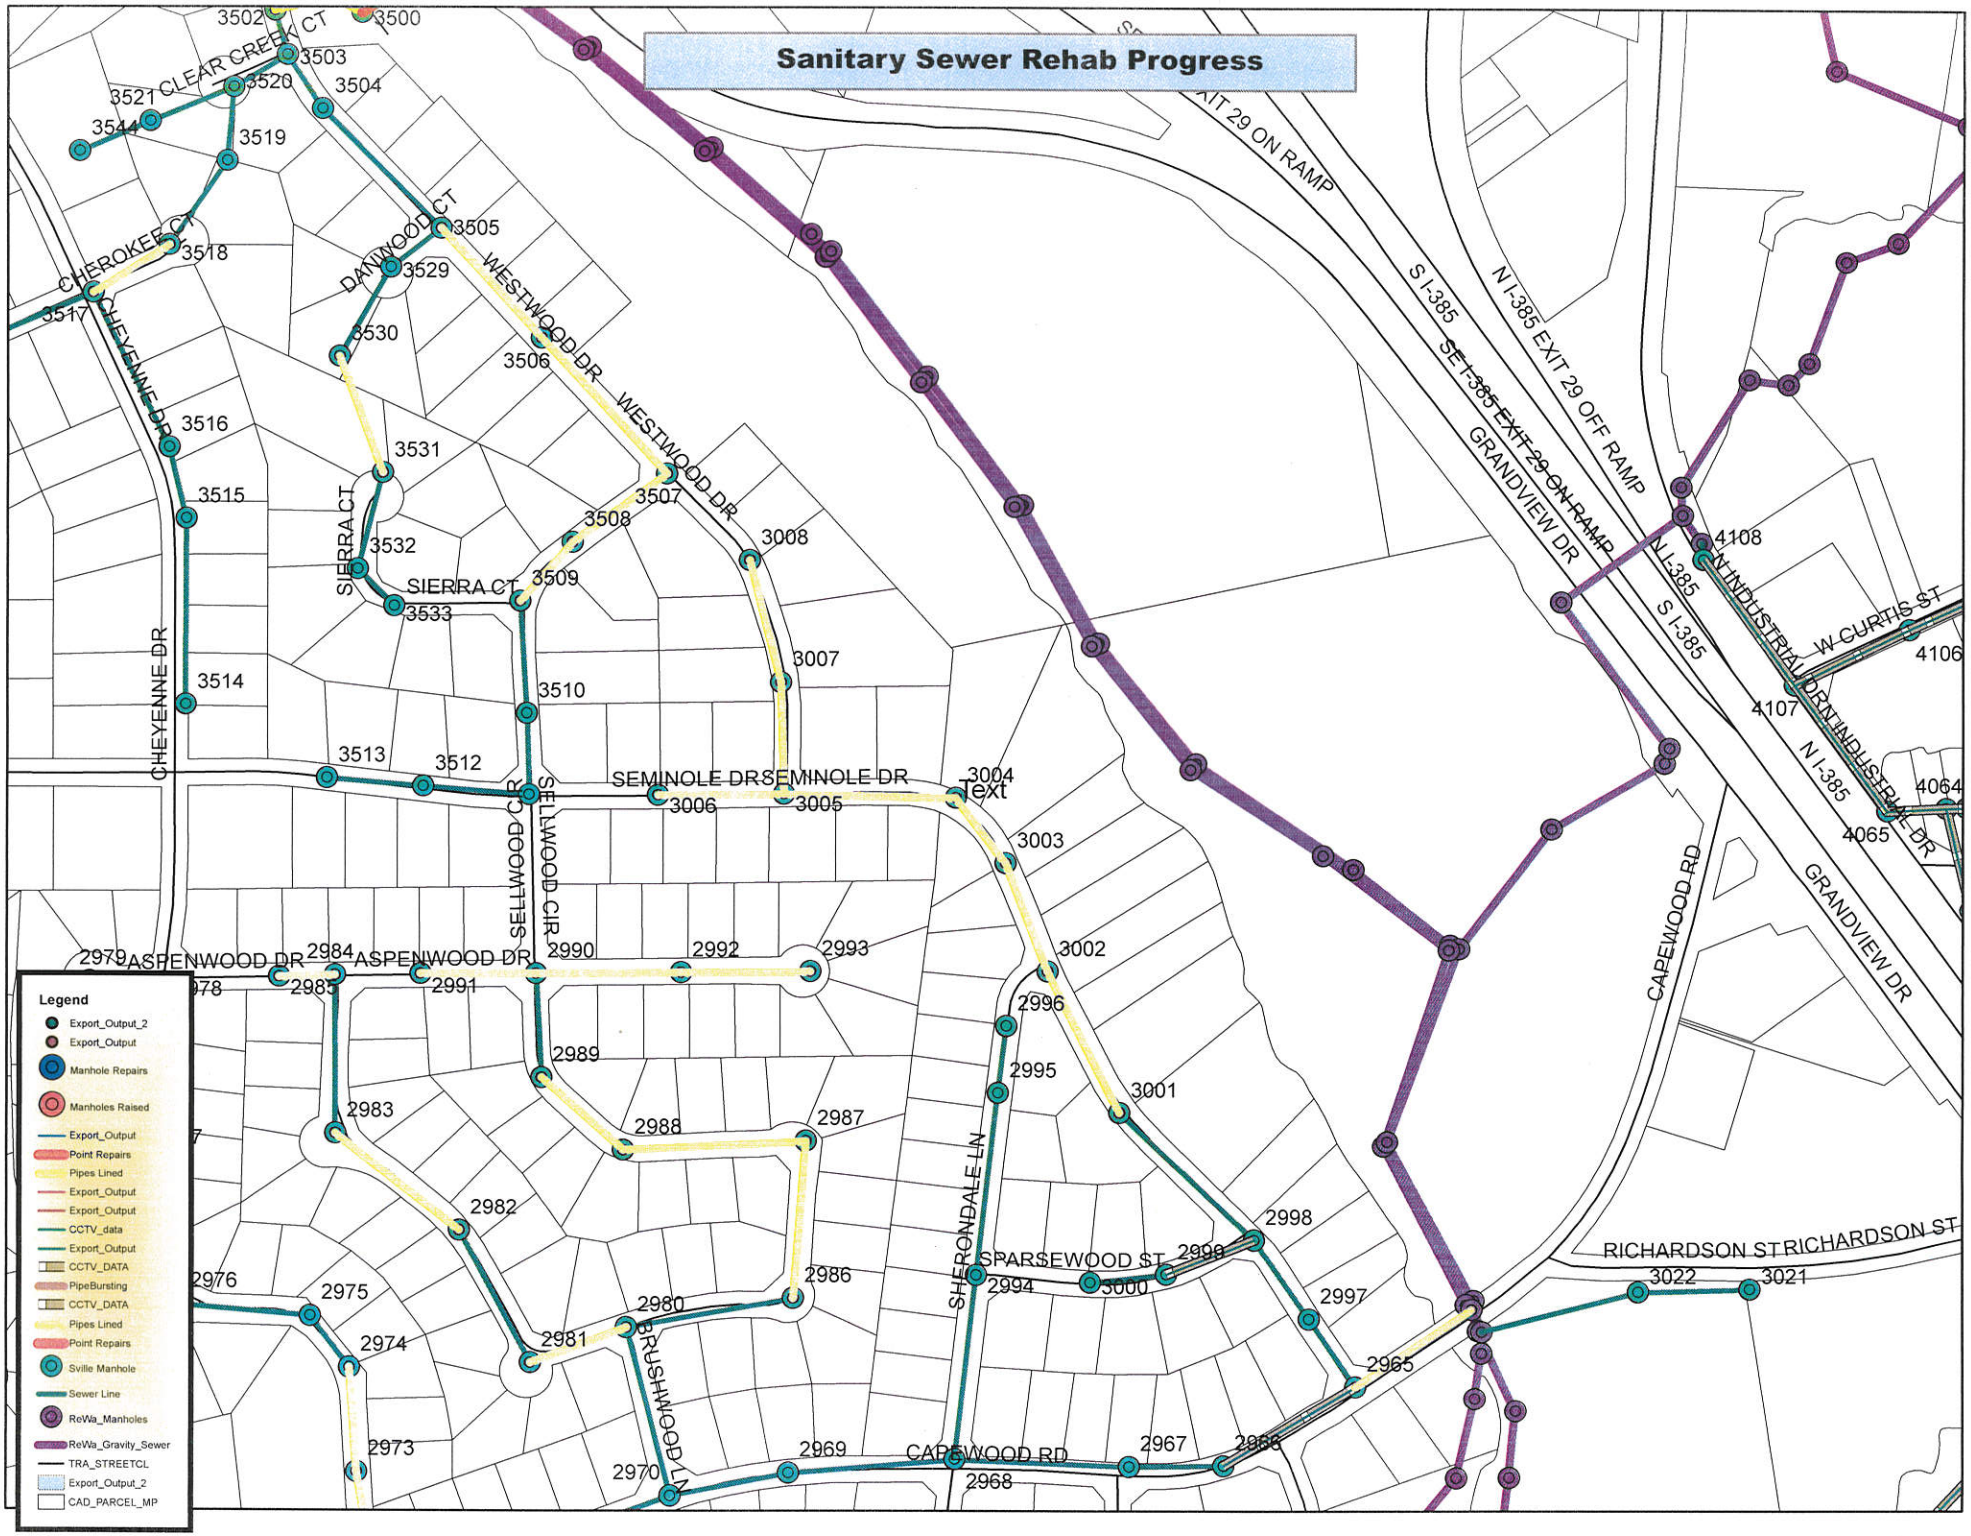
Sanitary Sewer Rehab Progress
Legend
Export_Output_2
Export_Output
Manhole Repairs
Manholes Raised
Export_Output
Point Repairs
Pipes Lined
Export_Output
Export_Output
CCTV_data
Export_Output
CCTV_DATA
PipeBursting
CCTV_DATA
Pipes Lined
Point Repairs
Sville Manhole
Sewer Line
ReWa_Manholes
ReWa_Gravity_Sewer
TRA_STREETCL
Export_Output_2
CAD_PARCEL_MP
CLEAR CREEK CT
CHEROKEE CT
CHEYENNE DR
DANWOOD CT
WESTWOOD DR
SIERRA CT
SEMINOLE DR
SELLWOOD CIR
ASPENWOOD DR
BRUSHWOOD LN
SHERONDALE LN
SPARSEWOOD ST
CAPEWOOD RD
RICHARDSON ST
GRANDVIEW DR
S I-385
N I-385
S I-385 EXIT 29 ON RAMP
N I-385 EXIT 29 OFF RAMP
W CURTIS ST
N INDUSTRIAL DR
Text

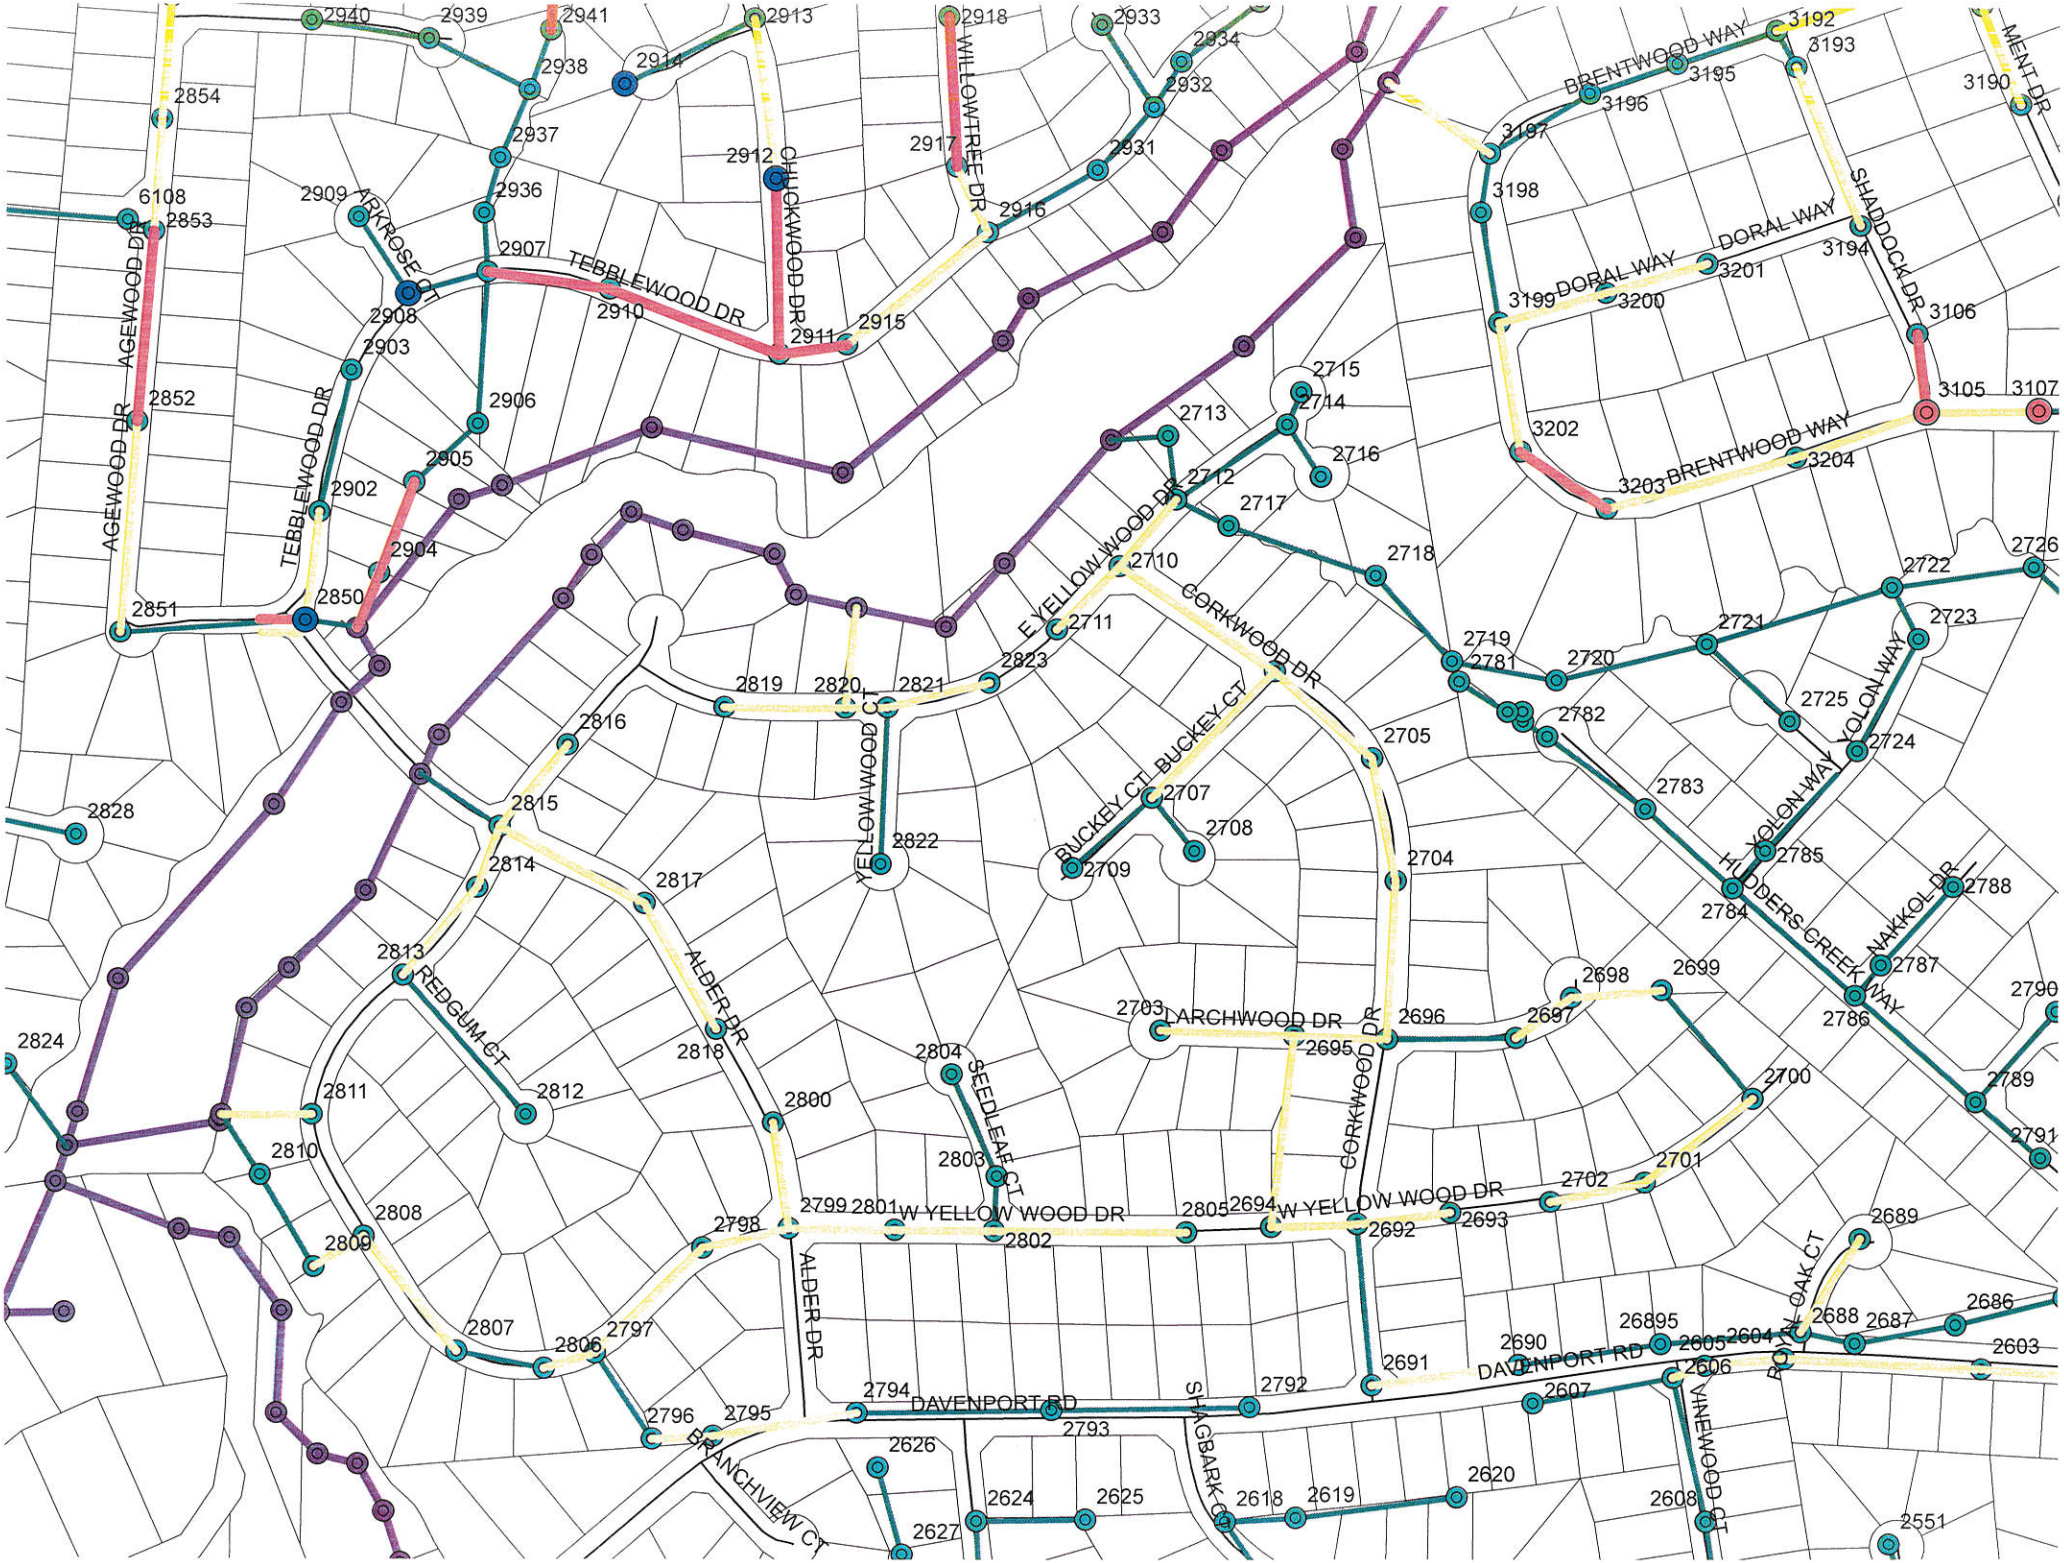

AGEWOOD DR
TEBBLEWOOD DR
ARKROSE CT
CHUCKWOOD DR
WILLOWTREE DR
BRENTWOOD WAY
DORAL WAY
SHADDOCK DR
MENT DR
E YELLOW WOOD DR
CORKWOOD DR
YELLOW WOOD CT
BUCKEY CT
YOLON WAY
HUDDERS CREEK WAY
NAKKOL DR
REDGUM CT
ALDER DR
LARCHWOOD DR
SEEDLEAF CT
W YELLOW WOOD DR
DAVENPORT RD
SHAGBARK CT
BRANCHVIEW CT
VINEWOOD CT
ROYAL OAK CT

IPR SOUTHEAST

## WEEKLY SCHEDULE

**2018 SIMPSONVILLE FY17/19 SS Rehab**

| | | | |
|---|---|---|---|
| CREW | IPR1 CIPP (Ulysses Franklin) | CREW | |
| WO # | | WO # | |
| CREW | IPR2 | CREW | P&H OC (Dennis Hollifield) (Roel)(Chris) |
| WO # | | WO # | |
| CREW | IPR3 CIPP | CREW | United Sewer TV (Danny Herrin) |
| WO # | | WO # | |
| CREW | Culy Contracting (MH Rehab) | CREW | Raintree TV (Eli) |
| WO # | | WO # | |

| MONDAY | Date: 10/1/2018 |
|---|---|
| CREW | DESCRIPTION OF WORK |
| IPR1 | CIPP: 3005_3004, Seminole Dr, Seminole W.O. |
| | CIPP: 3003_3001, Capewood Rd, Seminole W.O. |
| P&H1 | |
| P&H2 | Davenport W.O. |

| TUESDAY | Date: 10/2/2018 |
|---|---|
| CREW | DESCRIPTION OF WORK |
| IPR1 | CIPP: 2699_3697, Larchwood Rd, Davenport W.O. |
| | CIPP: 2819_2820, Yellowood Rd, Davenport W.O. |
| P&H1 | |
| P&H2 | Davenport W.O. |

| WEDNESDAY | Date: 10/3/2018 |
|---|---|
| CREW | DESCRIPTION OF WORK |
| IPR1 | CIPP: 2820_300B-143, Yellowood Rd, Davenport W.O. |
| | CIPP: 2965_REWA, Capewood Rd, Seminole W.O. |
| IPR T/C | |
| P&H1 | |
| P&H2 | Davenport W.O. |
| United Sewer | Basin 3 W.O. |

| THURSDAY | Date: 10/4/2018 |
|---|---|
| CREW | DESCRIPTION OF WORK |
| IPR1 | |

| | |
|---|---|
| | |
| IPR T/C | |
| | |
| P&H1 | |
| | |
| P&H2 | Davenport W.O. |
| | |
| | |
| United Sewer | |
| | |

| FRIDAY | Date: 10/5/2018 |
|---|---|
| WO# | DESCRIPTION OF WORK |
| | |
| IPR1 | |
| | |
| | |
| | |
| | |
| | |
| IPR T/C | |
| | |
| P&H1 | |
| | |
| P&H2 | Davenport W.O. |
| | |
| United Sewer | |
| | |

| SATURDAY | Date: 10/6/2018 |
|---|---|
| WO# | DESCRIPTION OF WORK |
| | No Crews |
| | |
| | |
| | |
| | |
| | |
| | |
| | |

| SUNDAY | Date: 10/7/2018 |
|---|---|
| WO# | DESCRIPTION OF WORK |
| | No Crews |
| | |
| | |
| | |
| | |
| | |
| | |
| | |
